ID	Task Name	Duration	Start	Finish
1	**PHASE IA**	**56 days**	**Tue 7/14/15**	**Tue 9/29/15**
2	RCB CULVERT	30 days	Tue 7/14/15	Mon 8/24/15
3	EXCAVATION	5 days	Tue 8/25/15	Mon 8/31/15
4	LIME STABILIZATION	5 days	Tue 9/1/15	Mon 9/7/15
5	CONCRETE PAVING	7 days	Tue 9/8/15	Wed 9/16/15
6	INLET TOPS	5 days	Thu 9/17/15	Wed 9/23/15
7	DRIVEWAYS	5 days	Thu 9/17/15	Wed 9/23/15
8	SIDEWALK & RAMPS	5 days	Thu 9/17/15	Wed 9/23/15
9	BACKFILL	3 days	Thu 9/24/15	Mon 9/28/15
10	SWITCH TRAFFIC	1 day	Tue 9/29/15	Tue 9/29/15
11				
12	**PHASE IB**	**49 days**	**Wed 9/30/15**	**Mon 12/7/15**
13	SANITARY SEWER	20 days	Wed 9/30/15	Tue 10/27/15
14	RCB CULVERT	30 days	Wed 9/30/15	Tue 11/10/15
15	EXCAVATION	5 days	Wed 10/28/...	Tue 11/3/15
16	LIME STABILIZATION	5 days	Wed 11/4/15	Tue 11/10/15
17	CONCRETE PAVING	7 days	Wed 11/11/...	Thu 11/19/15

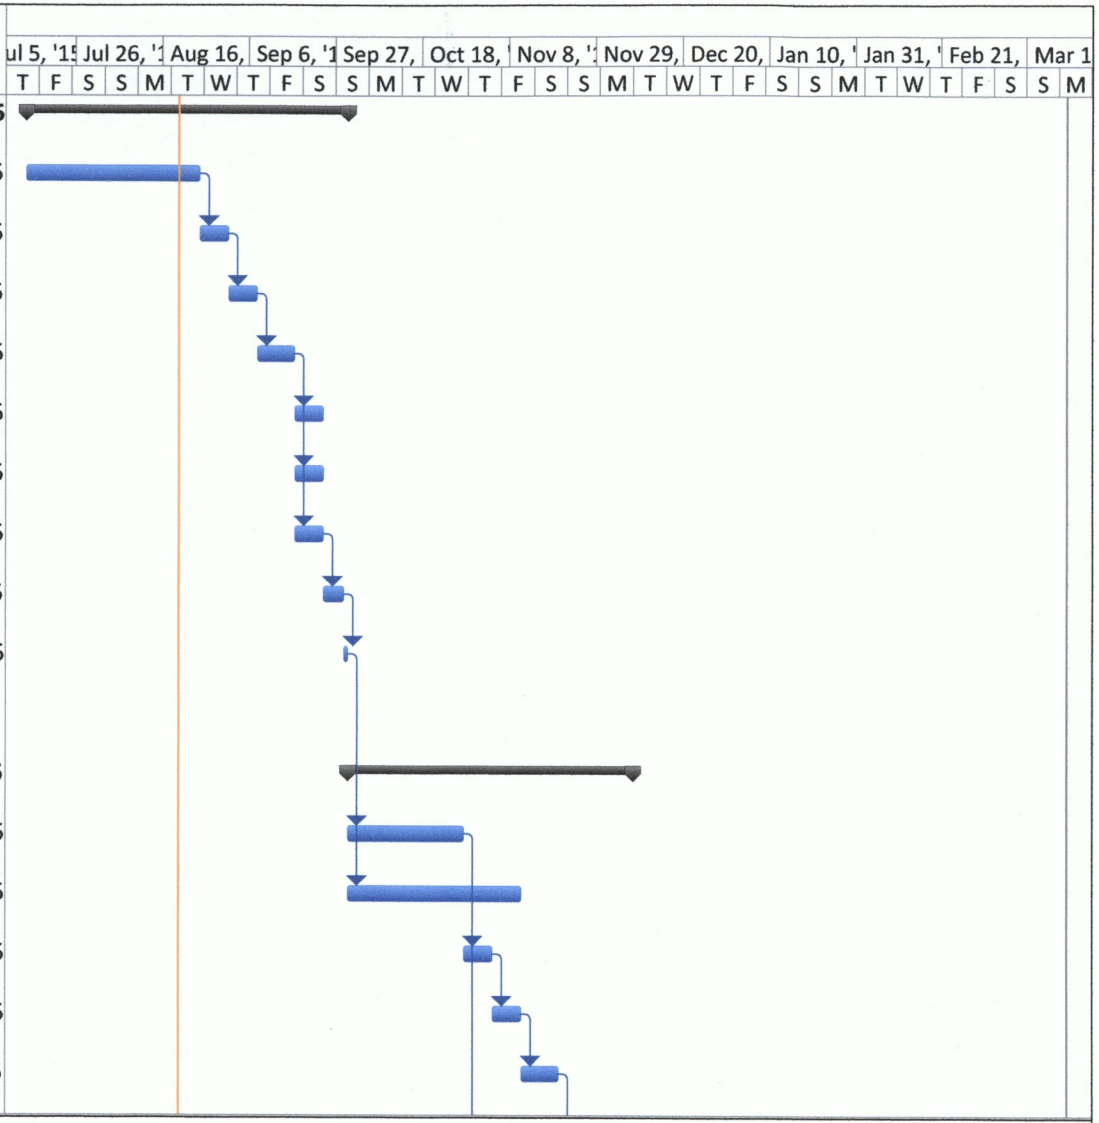

Project: Bethel & Coppell 82015
Date: Thu 8/20/15

Task	External Milestone	Manual Summary Rollup	
Split	Inactive Task	Manual Summary	
Milestone	Inactive Milestone	Start-only	
Summary	Inactive Summary	Finish-only	
Project Summary	Manual Task	Deadline	
External Tasks	Duration-only	Progress	

ID	Task Name	Duration	Start	Finish
18	INTERSECTIONS	5 days	Fri 11/20/15	Thu 11/26/15
19	INLET TOPS	5 days	Fri 11/20/15	Thu 11/26/15
20	DRIVEWAYS	5 days	Fri 11/20/15	Thu 11/26/15
21	SIDEWALK & RAMPS	5 days	Fri 11/20/15	Thu 11/26/15
22	BACKFILL	3 days	Fri 11/27/15	Tue 12/1/15
23	STRIPING & SIGNAGE	3 days	Wed 12/2/15	Fri 12/4/15
24	SWITCH TRAFFIC	1 day	Mon 12/7/15	Mon 12/7/15
25				
26	**PHASE 2A**	**76 days**	**Wed 10/28...**	**Wed 2/10/16**
27	PREP R.O.W.	5 days	Wed 10/28/...	Tue 11/3/15
28	WATER LINE	30 days	Wed 10/28/...	Tue 12/8/15
29	CLOSE NORTH SIDE	1 day	Tue 12/8/15	Tue 12/8/15
30	STORM DRAIN	15 days	Wed 12/9/15	Tue 12/29/15
31	EXCAVATION	5 days	Wed 12/30/...	Tue 1/5/16
32	LIME STABILIZATION	5 days	Wed 1/6/16	Tue 1/12/16
33	CONCRETE PAVING	7 days	Wed 1/13/16	Thu 1/21/16
34	INTERSECTIONS	5 days	Fri 1/22/16	Thu 1/28/16

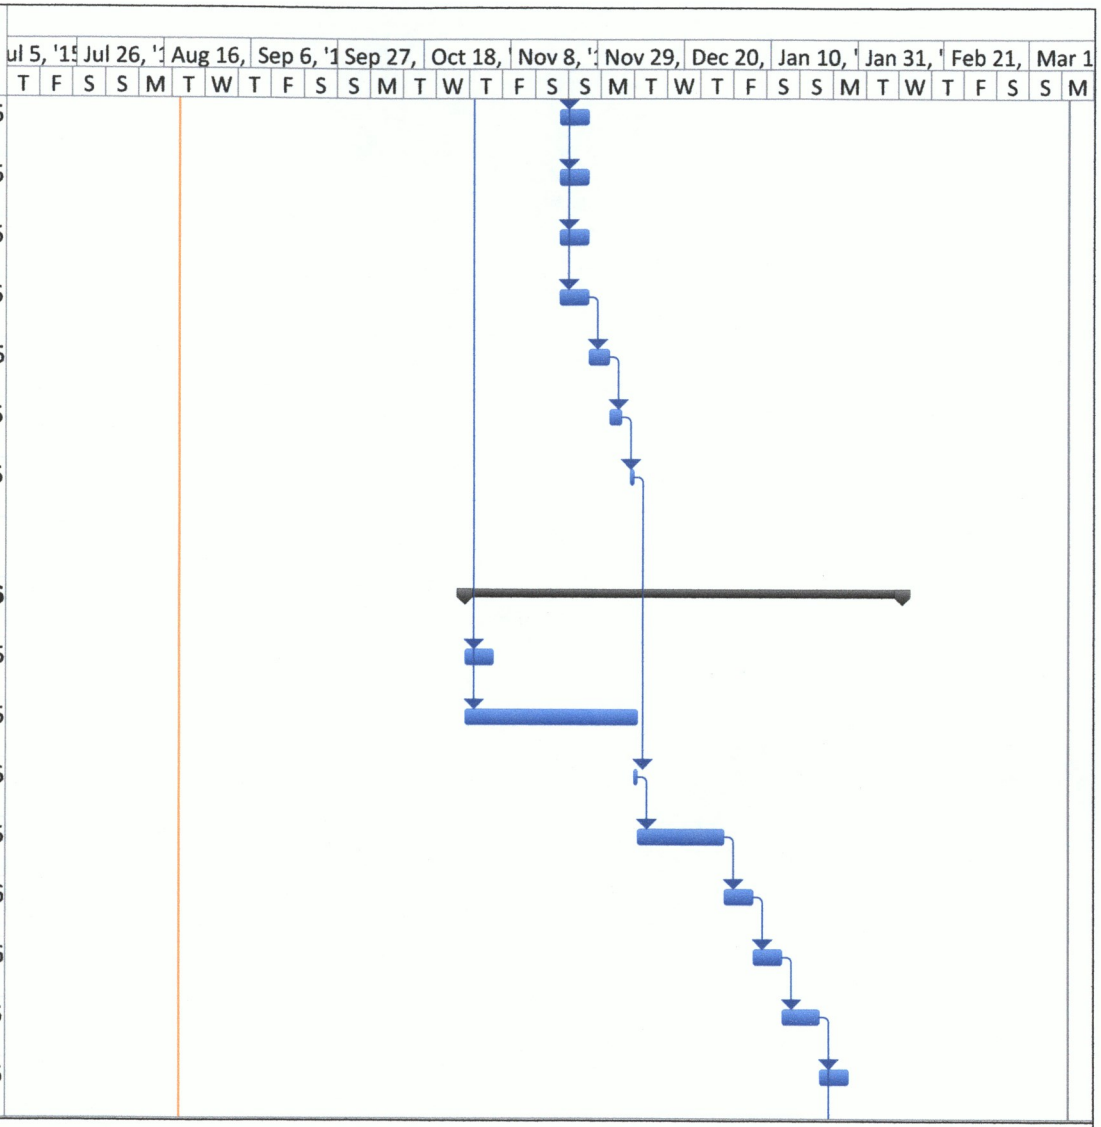

Project: Bethel & Coppell 82015
Date: Thu 8/20/15

Task	External Milestone	Manual Summary Rollup
Split	Inactive Task	Manual Summary
Milestone	Inactive Milestone	Start-only
Summary	Inactive Summary	Finish-only
Project Summary	Manual Task	Deadline
External Tasks	Duration-only	Progress

ID	Task Name	Duration	Start	Finish
35	INLET TOPS	5 days	Fri 1/22/16	Thu 1/28/16
36	DRIVEWAYS	5 days	Fri 1/22/16	Thu 1/28/16
37	SIDEWALK & RAMPS	5 days	Fri 1/29/16	Thu 2/4/16
38	BACKFILL	3 days	Fri 2/5/16	Tue 2/9/16
39	SWITCH TRAFFIC	1 day	Wed 2/10/16	Wed 2/10/16
40				
41	**PHASE 2B**	**29 days**	**Thu 2/11/16**	**Tue 3/22/16**
42	EXCAVATION	5 days	Thu 2/11/16	Wed 2/17/16
43	LIME STABILIZATION	5 days	Thu 2/18/16	Wed 2/24/16
44	CONCRETE PAVING	7 days	Thu 2/25/16	Fri 3/4/16
45	INTERSECTIONS	5 days	Mon 3/7/16	Fri 3/11/16
46	INLET TOPS	5 days	Mon 3/7/16	Fri 3/11/16
47	DRIVEWAYS	5 days	Mon 3/7/16	Fri 3/11/16
48	SIDEWALK & RAMPS	5 days	Mon 3/7/16	Fri 3/11/16
49	BACKFILL	3 days	Mon 3/14/16	Wed 3/16/16
50	STRIPING & SIGNAGE	3 days	Thu 3/17/16	Mon 3/21/16
51	SWITCH TRAFFIC	1 day	Tue 3/22/16	Tue 3/22/16

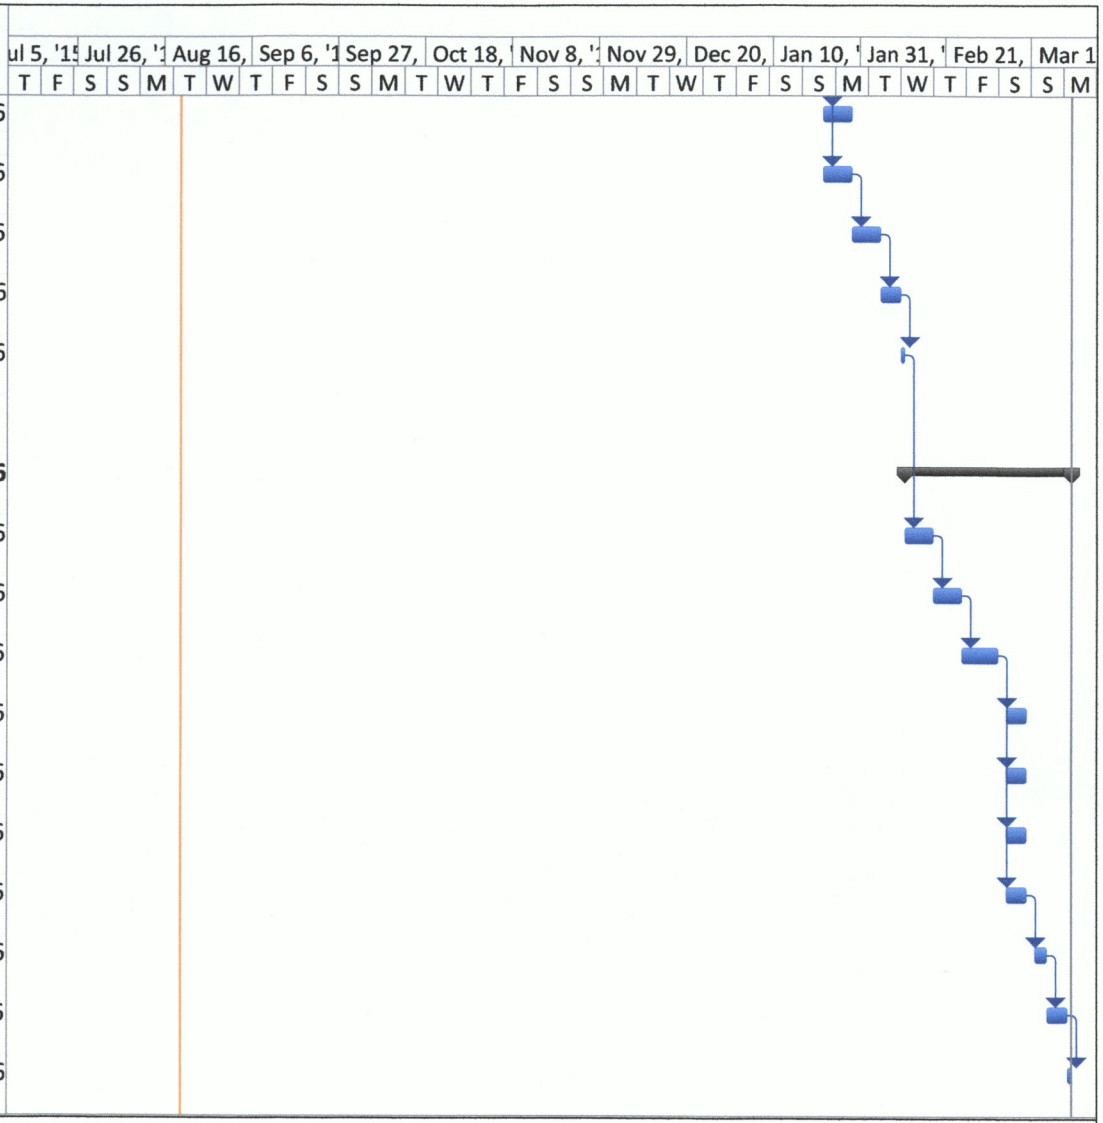

Project: Bethel & Coppell 82015
Date: Thu 8/20/15

Task	External Milestone	Manual Summary Rollup	
Split	Inactive Task	Manual Summary	
Milestone	Inactive Milestone	Start-only	
Summary	Inactive Summary	Finish-only	
Project Summary	Manual Task	Deadline	
External Tasks	Duration-only	Progress	
